





ID	Task Name	Duration	Start	Finish	Qtr 3, 2003			Qtr 4, 2003			Qtr 1, 2004			Qtr 2, 2
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
1	Data Collection	8 days	Thu 21/08/03	Mon 1/09/03										
2	Import Telstra (fixed) call details	4 days	Thu 21/08/03	Tue 26/08/03										
3	Import Telstra (fixed) rent details	1.5 days	Wed 27/08/03	Thu 28/08/03										
4	Import Telstra (fixed) other details	1 day	Fri 29/08/03	Fri 29/08/03										
5	Refine tDataCollection structure after 2-4	1 day	Sat 30/08/03	Mon 1/09/03										
6	Batch Processing	6 days	Tue 2/09/03	Tue 9/09/03										
7	Create summary view for user processing	6 days	Tue 2/09/03	Tue 9/09/03										
8	SQL	6 days	Tue 2/09/03	Tue 9/09/03										
9	Screen Layout	6 days	Tue 2/09/03	Tue 9/09/03										
10	Access to details	6 days	Tue 2/09/03	Tue 9/09/03										
11	Critical Errors	6 days	Tue 2/09/03	Tue 9/09/03										
12	Create Batch screen and underlying code (Telstra)	4 days	Wed 10/09/03	Mon 15/09/03										
13	Handling of Critical Error decisions	4 days	Tue 16/09/03	Fri 19/09/03										
14	Refine tDataCollection structure	2 days	Mon 22/09/03	Tue 23/09/03										
15	Refine tTransaction structure	2 days	Wed 24/09/03	Thu 25/09/03										
16	Create summary view for user processing	6 days	Fri 26/09/03	Fri 3/10/03										
17	SQL	6 days	Fri 26/09/03	Fri 3/10/03										
18	Screen Layout	6 days	Fri 26/09/03	Fri 3/10/03										
19	Access to details	6 days	Fri 26/09/03	Fri 3/10/03										
20	Critical Errors	6 days	Fri 26/09/03	Fri 3/10/03										
21	Create Batch screen and underlying code (Telstra)	4 days	Mon 6/10/03	Thu 9/10/03										
22	Handling of Dubious Record decisions	6 days	Fri 10/10/03	Fri 17/10/03										
23	By selection	6 days	Fri 10/10/03	Fri 17/10/03										
24	Clear all	6 days	Fri 10/10/03	Fri 17/10/03										
25	On acceptance of the bill	6 days	Fri 10/10/03	Fri 17/10/03										
26	Refine tTransaction structure after 11-13	1 day	Fri 10/10/03	Fri 10/10/03										
27	Refine tProcessedTransaction structure after 11-14	1 day	Mon 13/10/03	Mon 13/10/03										
28	Transfer and expand data into tProcessedTransaction	3 days	Tue 14/10/03	Thu 16/10/03										
29	Transfer summary data to TBS	3 days	Fri 17/10/03	Tue 21/10/03										
30	Refine summary table structure after 16-17	1 day	Wed 22/10/03	Wed 22/10/03										
31	Other Import Suppliers	3 days	Thu 23/10/03	Mon 27/10/03										

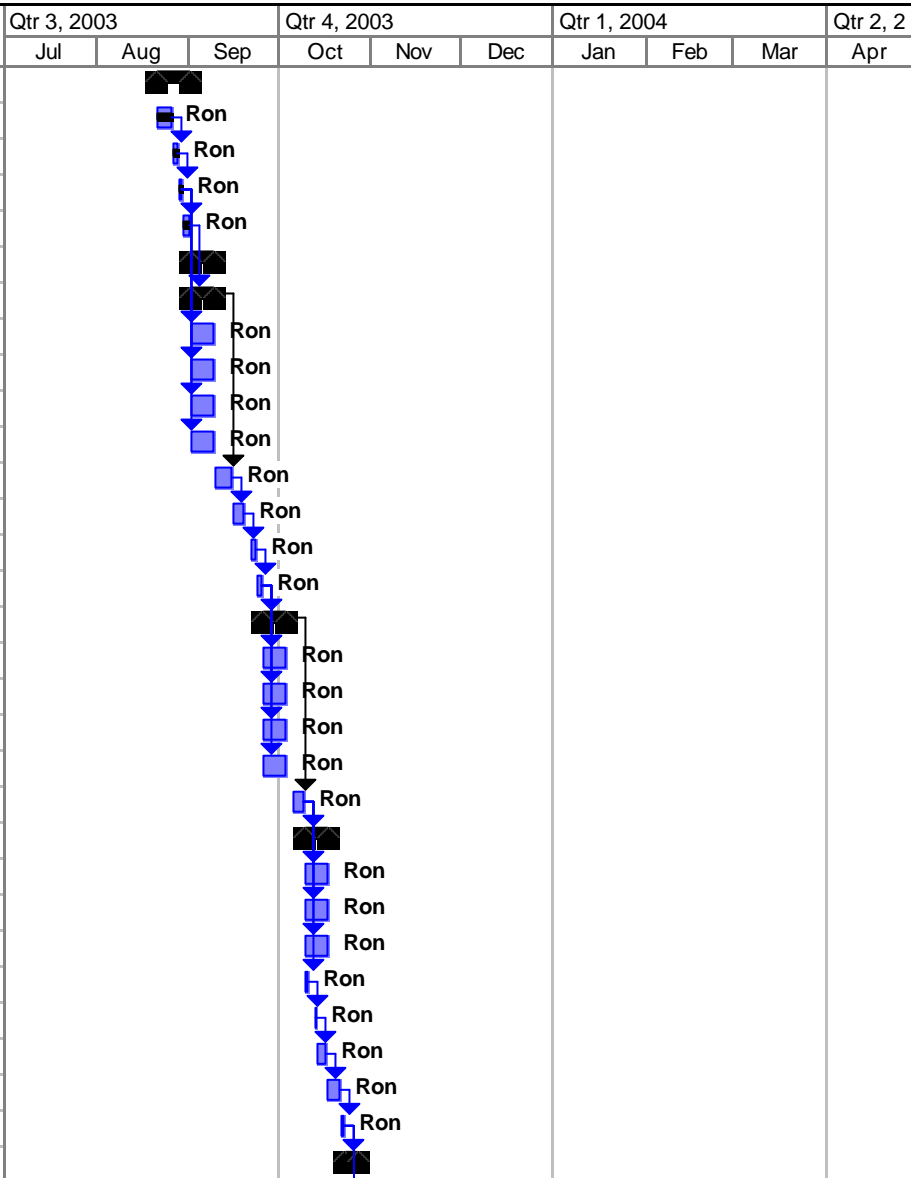

Project: PPDevelopment Date: Fri 5/09/03	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Qtr 3, 2003			Qtr 4, 2003			Qtr 1, 2004			Qtr 2, 2
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
32	AAPT Import	2 days	Thu 23/10/03	Fri 24/10/03					Ron					
33	Telmax Import	2 days	Thu 23/10/03	Fri 24/10/03					Ron					
34	Optus Import	3 days	Thu 23/10/03	Mon 27/10/03					Ron					
35	Import Telstra Mobile	2 days	Thu 23/10/03	Fri 24/10/03					Ron					
36	Vodafone	2 days	Thu 23/10/03	Fri 24/10/03					Ron					
37	Other Tasks	92 days	Mon 27/10/03	Tue 2/03/04										
38	Enhancements	10 days	Mon 27/10/03	Fri 7/11/03					Ron					
39	Maintenance Screens	5 days	Mon 10/11/03	Fri 14/11/03					Ron					
40	SQL Conversion and Testing	2 days	Mon 17/11/03	Tue 18/11/03					Ron					
41	Users and Security	3 days	Wed 19/11/03	Fri 21/11/03					Ron					
42	Documentation	10 days	Mon 24/11/03	Fri 5/12/03					Ron					
43	System Testing	10 days	Mon 8/12/03	Fri 19/12/03					Ron					
44	User Acceptance Testing	20 days	Mon 22/12/03	Fri 16/01/04					Ron					
45	Audit Functions	10 days	Mon 19/01/04	Fri 30/01/04					Ron					
46	Annual Charges	10 days	Mon 2/02/04	Fri 13/02/04					Ron					
47	Manual Input	6 days	Mon 16/02/04	Mon 23/02/04					Ron					
48	Service Records	6 days	Tue 24/02/04	Tue 2/03/04					Ron					

Project: PPDevelopment Date: Fri 5/09/03	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
